Counter Taobao Weekly Update

Week ending 2 May 2025

ERP initiative

[Progress] In progress with integration with 聚水潭 and 旺店通 (ETA mid-May)

Key updates

1. **System integration in progress:** 聚水潭 and 旺店通 have both given us sample TB/PDD data for our product team to work on; ETA still targeted mid-May
2. **Impact Assessment:** Updated in next page

Completed | In progress | Planned, to start | Delayed

Topic	#	Task	PIC	Status
ERP Info	1	Collect ERP account information from sellers	Siri	Completed
	2	Check the completeness of the information provided from ERP e.g. stock, price, PO	Siri/Monica	Completed
	3	Collect TB price from sellers	Keith	Paused
	4	Check if TB price matches with price in 聚水潭	Siri/Monica	Completed
Other ERPs	5	Start discussions with 旺店通	Ivy/Gerold	Completed
Feasibiliy Checks	6	Product feasibility check with individual product lines	Monica	Completed
	7	Provide a product solution proposal	Monica	Completed
	8	Ensure that Legal/Finance has a ToS for sellers to sign	Monica/Cuiwei	Completed
	9	Confirmation if 聚水潭 is willing to work with us	Gerold	Completed
Commercial	10	Map out business flow with BPMs	Monica/Cuiwei	Completed
	11	聚水潭 to provide seller information e.g. # sellers, # listings, etc	Gerold	Paused
	12	Estimate business impact with data from 聚水潭	Lynn/Nic	Completed
	13	High level summary of partnership between SHP and 聚水潭	Lynn/Nic	Completed
Implementation	14	Get list of cooperative sellers	Siri	Completed
	15	Ensure that system flow is sorted out e.g. listing, pricing, operations, arranging of shipment, escrow, etc	Siri/Monica	Completed
	16	Start trial with cooperative sellers	Monica	Paused
	17	聚水潭 and 旺店通 to integrate with our API	Monica	In Progress
	18	To confirm working-level flow between SHP and 聚水潭	Gerold/Siri	In Progress

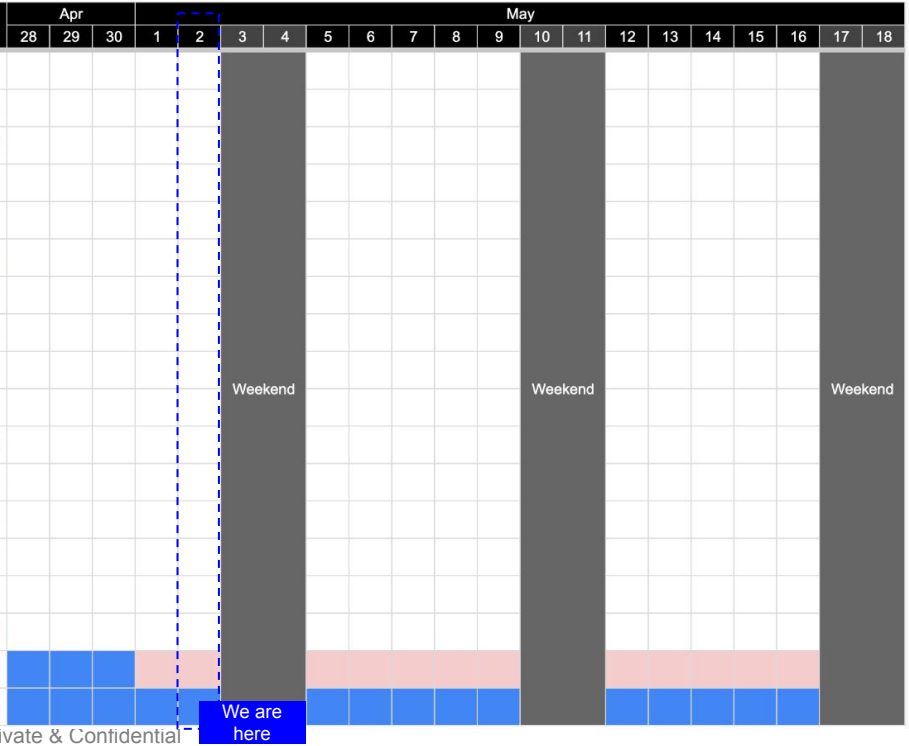

[Impact estimate] Expected uplift of between 1.1-3.3x on top of existing ADO and SKU# from integration with both ERPs

Table: Expected uplift from 2 ERPs 聚水潭 & 旺店通

Scenario	Conservative	Aggressive
Total ADO after uplift	**72,930**	**148,783**
... Apr MTD ADO	35,004	35,004
... Uplift	**37,926**	**113,779**
... Uplift (%)	108%	325%
Total SKU # after uplift	**1,684,118**	**3,435,718**
... Apr MTD SKU #	808,318	808,318
... Uplift	**875,800**	**2,627,400**
... Uplift (%)	108%	325%

Assumptions:

1. Seller pitching success 15-30% & SKU migration 48-72% for each scenario respectively
2. SKU effi assumes current SKU effi for all SKUs
3. 聚水潭's SKU# is calculated based on CN's estimations of 聚水潭 vs 旺店通 by category

Highlights:

1. **ADO and SKU# expected to increase 1.1x - 3.3x in each scenario respectively:** ADO expected to increase between 37k-113k depending on scenario, and SKU# between 0.9 - 2.6 mil

Fashion Update

[Fashion Progress: existing program seller] This week, we are working with BI to expand our performance tracking to all TB sellers + SKUs (vs currently only tracking program); sourcing targets/wishlist in progress

Completed | In progress | To start | Delayed

Market	Topic	#	Task	PIC	Status
Cross-migrate existing TB SKUs on Shopee platform to SG, MY, TH, VN, TW & PH					
SG	Commercial	1	Align potential migration pool	Tina	Completed
		2	Marketing resources alignment	Tina	Completed
		3	Align SKU migration target, acquisition target and	Tina/Lynn	Completed
		4	Conduct seller pitching	Lynn	Completed
		5	Support seller onboarding / SKU listing / migration	Lynn	In Progress
		6	Conduct marketing push	Tina	In Progress
MY	Commercial	7	Align potential migration pool	Max	Completed
		8	Marketing resources alignment	Max	Completed
		9	Align SKU migration target, acquisition target and	Max/Lynn	Completed
		10	Conduct seller pitching	Lynn	Completed
		11	Support seller onboarding / SKU listing / migration	Lynn	In Progress
		12	Conduct marketing push	Max	In Progress
TH	Commercial	13	Align potential migration pool	Tiffany	Completed
		14	Marketing resources alignment	Tiffany	Completed
		15	Align SKU migration target, acquisition target and	Tiffany/Lynn	Completed
		16	Conduct seller pitching	Lynn	Completed
		17	Support seller onboarding / SKU listing / migration	Lynn	In Progress
		18	Conduct marketing push	Tiffany	In Progress
VN	Commercial	19	Align potential migration pool	Eric	Completed
		20	Marketing resources alignment	Eric	Completed
		21	Align SKU migration target, acquisition target and	Eric/Lynn	Completed
		22	Conduct seller pitching	Lynn	Completed
		23	Support seller onboarding / SKU listing / migration	Lynn	In Progress
		24	Conduct marketing push	Eric	In Progress
TW	Commercial	25	Align potential migration pool	Amanda	Completed
		26	Marketing resources alignment	Amanda	Completed
		27	Align SKU migration target, acquisition target and	Amanda/Lynn	Completed
		28	Conduct seller pitching	Lynn	Completed
		29	Support seller onboarding / SKU listing / migration	Lynn	In Progress
		30	Conduct marketing push	Amanda	In Progress
PH	Commercial	31	Align potential migration pool	Ashley	Completed
		32	Marketing resources alignment	Ashley	Completed
		33	Align SKU migration target, acquisition target and	Ashley/Lynn	Completed
		34	Conduct seller pitching	Lynn	Paused
		35	Support seller onboarding / SKU listing / migration	Lynn	Paused
		36	Conduct marketing push	Ashley	In Progress
All	Commercial	37	Identify more TB SHP sellers via broadcasting	Lynn	Completed
		38	Market review and selection of sellers	All	Completed
		39	Conduct seller pitching	Lynn	In Progress
		40	Add successful sellers into existing pool	Lynn	In Progress

Highlights

- **Universe view data being worked on by BI and us:** To show performance from all identified TB sellers + SKUs (vs current view of only program sellers + SKUs) by next monthly meeting
- **Sourcing targets and wishlist in progress:** Target alignment in progress with CN (ETA 7 May), LVT (9 May), SCS (22 May). Wishlist quality being improved together with BI.

[Fashion Progress: new top TB seller acquisition] 27-36 sellers successfully acquired across all markets in Mar/Apr; 4-11 sellers in latest Apr batch to be added into program from 6 May

Completed | In progress | To start | Delayed

Market	Topic	#	Task	PIC	Status
Acquire top TB sellers / SKUs that are not on SHP					
		42	Sellers review	Tina	Completed
		43	Marketing resource alignment	Tina	Completed
		44	Conduct seller pitching	Lynn	In Progress
		45	Seller onboarding and SKU listing/migration	Lynn	In Progress
SG	Commercial	46	Marketing push	Tina	In Progress
		47	Sellers review	Max	Completed
		48	Marketing resource alignment	Max	Completed
		49	Conduct seller pitching	Lynn	In Progress
		50	Seller onboarding and SKU listing/migration	Lynn	In Progress
MY	Commercial	51	Marketing push	Max	In Progress
		52	Sellers review	Tiffany	Completed
		53	Marketing resource alignment	Tiffany	Paused
		54	Conduct seller pitching	Lynn	In Progress
		55	Seller onboarding and SKU listing/migration	Lynn	In Progress
TH	Commercial	56	Marketing push	Tiffany	In Progress
		57	Sellers review	Eric	Completed
		58	Marketing resource alignment	Eric	Completed
		59	Conduct seller pitching	Lynn	In Progress
		60	Seller onboarding and SKU listing/migration	Lynn	In Progress
VN	Commercial	61	Marketing push	Eric	In Progress
		62	Sellers review	Amanda	Completed
		63	Marketing resource alignment	Amanda	Completed
		64	Conduct seller pitching	Lynn	In Progress
		65	Seller onboarding and SKU listing/migration	Lynn	In Progress
TW	Commercial	66	Marketing push	Amanda	To start
		67	Sellers review	Ashley	Completed
		68	Marketing resource alignment	Ashley	Completed
		69	Conduct seller pitching	Lynn	In Progress
		70	Seller onboarding and SKU listing/migration	Lynn	To start
PH	Commercial	71	Marketing push	Ashley	To start

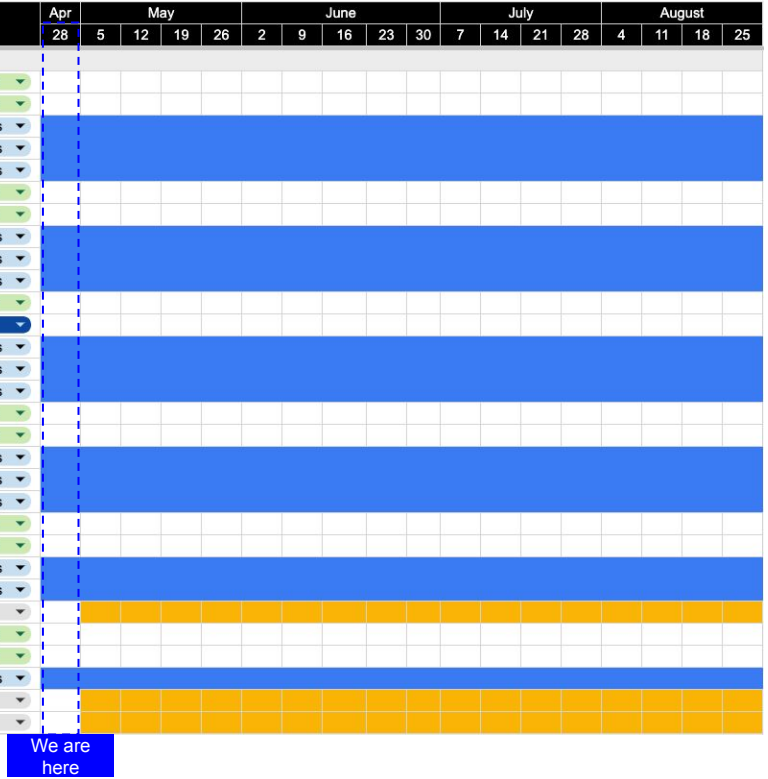

Highlights

[VN, TH, TW, SG, MY]

- Since start of acquisition, we have **acquired 27-36 sellers in each mkt**
- In Apr, 4-11 sellers successfully acquired across all markets and will be added to program by 6 May
- Remaining sellers not selected by market or rejected to join program will be pitched to join via CNSIP [ETA: Mid-May]

[Fashion Progress: Crawled and matched Taobao SKUs on Shopee] To re-crawl from TB by end of next week to improve sourcing wishlist quality

Completed | In progress | To start | Delayed

Market	Topic	#	Task	PIC	Status
Crawl and match top TB SKUs on SHP					
SG	Commercial	72	Crawl TB LZD SKUs	Keith	Completed
		73	Mapping to existing SHP SKUs	Keith	Completed
		74	Selection of SKUs	Tina	Completed
		75	Marketing resource alignment	Tina	Completed
		77	Marketing push	Tina	In Progress
MY	Commercial	78	Crawl TB LZD SKUs	Keith	Completed
		79	Mapping to existing SHP SKUs	Keith	Completed
		80	Selection of SKUs	Max	Completed
		81	Marketing resource alignment	Max	Completed
		83	Marketing push	Max	In Progress
TH	Commercial	84	Crawl TB LZD SKUs	Keith	Completed
		85	Mapping to existing SHP SKUs	Keith	Completed
		86	Selection of SKUs	Tiffany	Completed
		87	Marketing resource alignment	Tiffany	Completed
		89	Marketing push	Tiffany	In Progress
VN	Commercial	90	Crawl TB LZD SKUs	Keith	Completed
		91	Mapping to existing SHP SKUs	Keith	Completed
		92	Selection of SKUs	Eric	Completed
		93	Marketing resource alignment	Eric	Completed
		95	Marketing push	Eric	In Progress

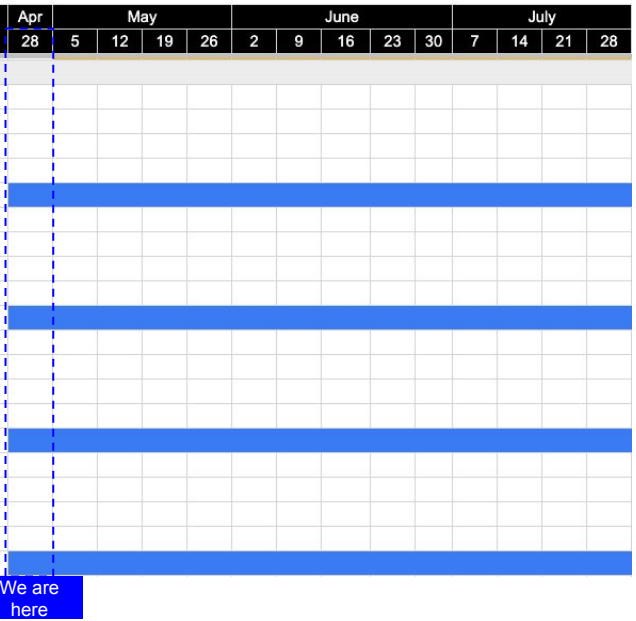

Highlights

To recrawl SKUs from TB by end of next week: Previously for fashion, we crawled LZD Taofashion due to seasonality. But to improve sourcing wishlist quality, we'll recrawl from TB

[Fashion Performance] Apr ADO 29.3k (MoM +0.5%, RR 114%); ADG $315k (MoM +2.3%, %CB grew across all mkts); PC2 2.5% (+0.8% vs CB); SKU# 523k (MoM +8.2%)

Table: Overall regional performance for 78 TB sellers in the program (Apr full month)

			All Markets	SG	MY	TW	PH	TH	VN
ADO	MTD(Apr)		29,369	743	4,082	240	11,087	7,099	6,117
	M-1(Mar)		29,225	683	4,605	225	13,383	5,520	4,808
	MoM		0.5%	8.7%	-11.4%	6.8%	-17.2%	28.6%	27.2%
	RR		114%	86%	104%	124%	110%	130%	115%
	CB% MTD		4.3%	2.2%	3.8%	1.2%	5.5%	6.1%	3.0%
	CB% MoM	1	0.4%	0.3%	0.3%	0.2%	-0.4%	1.8%	0.7%
ADG	MTD		$314,659	$10,224	$45,546	$5,453	$127,951	$68,780	$56,705
	MoM		2.3%	7.3%	-1.0%	6.6%	-5.0%	10.2%	13.7%
	CB% MTD		7.2%	2.7%	4.7%	1.1%	12.4%	9.9%	6.8%
	CB% MoM	2	0.7%	0.4%	0.5%	0.1%	0.1%	1.7%	0.9%
ABS	MTD		$11	$14	$11	$23	$12	$10	$9
	MoM		1.8%	-1.3%	11.7%	-0.2%	14.7%	-14.3%	-10.6%
PC2 %	MTD		2.5%	7.4%	1.0%	10.5%	1.4%	2.5%	4.4%
	MoM	3	0.5%	-0.8%	-0.1%	-0.4%	1.6%	-0.8%	0.6%
	CB PC2		1.7%	8.1%	1.8%	7.1%	0.5%	-0.9%	-1.1%
	Delta		0.8%	-0.7%	-0.8%	3.4%	0.9%	3.4%	5.5%
# SKUs	MTD		522,794	60,249	68,221	40,674	158,009	99,915	95,726
	MoM	3	8.2%	4.1%	14.0%	11.9%	3.9%	11.9%	9.2%
	RR		107%	98%	103%	103%	118%	105%	103%
SKU effi	MTD		5.62%	1.23%	5.98%	0.59%	7.02%	7.11%	6.39%
	MoM	4	-7.1%	4.1%	-22.3%	-4.6%	-20.2%	15.0%	16.5%
	RR		106%	88%	101%	120%	93%	123%	112%

Highlights

1. Reg MTD ADO 29.4k (+0.5% MoM, **ADO% CB increased 0.4pp**)
   - MY drop due to MY CB decline in Apr vs Mar, but %CB grew 0.3%
   - PH drop due to overall rebate cut e.g. removal of FS0, hence ABS grew 15%
   - VN/TH increase due to addition of matched crawled SKUs
2. Reg MTD ADG $315k (+2.3% MoM); ADG as %CB +0.7% MoM - **ADG% CB grew for all mkts**
3. PC2 2.5%; +0.8% with CB PC2; local's plan to drop PC2 in Apr was not effective for some mkts e.g. SG/TW; re-working with mkts on their plan again (SG to do more item rebate)
4. SKU # 523k (+8.2% MoM); SKU count healthy across all mkts

[Fashion] Summary of focus initiatives (key changes from last update in blue)

Domain	#	Initiative	Description	Status	ETA
Grow SKU count	1	Self-Run Seller SKU cross-migration/new upload	Sellers to migrate/newly add SKUs via self-listing or migration tool	263k SKUs are added to local markets since program start Apr total SKU# RR: SG: 94% RR, MY: 99% RR, TH: 97% RR, VN: 103% RR, TW: 101% RR 30k SKUs pending migration, target completion by Jun'25	Jun'25
	2	Acquire TB sellers (top + non-top)	To acquire sellers from top 300 TB wishlist (not on SHP)	Apr batch: 4-11 sellers successfully acquired across all markets and will be added to program by 6 May Sellers that rejected and not selected by markets will be invited to join via CNSIP	Mid May
	3	Acquire new TB sellers (TB ERP)	To evaluate feasibility of acquiring sellers / SKUs via CN's top ERP 聚水潭/旺店通	Details updated in slides #3 and #4	Apr-May
	4	Crawling from LZD/TB	Crawl top fashion TB SKUs from LZD/TB	All mkts: To recrawl from TB (instead of LZD) to improve matching and sourcing wishlist quality	Mid May
	5	Source SKUs	Develop a regional wishlist for sellers, LVT and SCS to source	To recrawl SKUs from TB by end of next week for regional wishlist; Targets and incentive packages delayed to be aligned by next week, and sourcing to start the week after	Apr-May
	6	Identify more existing TB SHP sellers	Allow sellers on SHP to self reach out to join TB programme if they are TB sellers with proof provided	Total of 91 sellers identified, markets completed review. 1. [Sellers existing in markets] Added into program from 1st May 2. [Sellers not in market] Pitching to start from 6 May Next steps: To conduct a second round of broadcasting to identify new batch of sellers	Apr-May Deep-dive
Improve SKU effi	7	AMS + Livestream (Marketing Booster)	Marketing booster package set-up for SG/MY, comprising of livestream + AMS	Self-Run/CNSIP: SG/MY started in Mar; MY will continue into Apr, SG will pause due to poor performance	Apr
	8	Seller Investment	Seller to commit to all criterias set by markets to receive SHP's commitment	% of shops that fulfilled all commitments: SG 8%, MY 27%, TH 14%, VN 4% % of shops that fully expensed free ads credit: SG 87%, MY 92%	End Apr

6 [SKU supply increase plan] Through broadcast channels, 91 existing SHP sellers are identified with 13k ADO regionally

Table 1: Seller and Shop breakdown in terms of TB Annual GMV (RMB)

GMV (RMB) per year	# of GGP	# of Shop
Above 50mil	6	29
Between 10mil - 50mil	8	345
Between 100 - 10mil	18	48
Below 1mil	59	214
Total	**91**	**636**

Next slide for more details

Table 2: MTD shop performance by Market

Market	# of Shops	MTD ADG (USD)	MTD ADO
SG	85	$1,987	285
MY	115	$5,169	758
TH	122	$18,148	3,766
VN	104	$16,198	4,171
PH	136	$18,045	4,045
TW	74	$1,448	102
Total	**636**	**$60,994**	**13,127**

Highlights

- 91 TB existing SHP sellers are identified through 6 broadcasting channels (Announcement, Popup, Banner, SEH, WeChat and RM internal nomination)
- Overall combined MTD ADO at 13k and ADG $61k across all markets
- Markets reviewed all sellers and selected based on each market's needs, sellers existing in each market have been added into the program [Refer to next slide for more details]

6 [Existing TB sellers on SHP Pitching]: Sellers existing in markets and selected (12-27 sellers) have been added into the program from 1st May, remaining sellers to be pitched from 6 May

Table: Existing TB sellers on SHP Pitching

	Status	SG	MY	TH	VN	TW
1	Total sellers pool # [a] + [b]	91	91	91	91	91
	... Existing in market # [a]	30	45	46	34	53
	..... Selected by market to provide marketing push	12	17	16	27	22
2	... Not existing in market # [b]	61	46	45	57	38
	..... Selected by market to acquire into market	33	22	37	31	10

Highlights

1 Out of pool of 91 sellers, 30-53 sellers already have presence in each local mkt; of which, **mkts selected 12-27 sellers to push**

2 For those sellers who have no presence in the mkt, to pitch if mkt selects them (ETA start 6 May)

6

[Backup: Existing in mkt sellers on SHP Pitching]: Markets selection rate ranges from 37% to 79% to include shops already in market into program hitlist

Status	SG	MY	TH	VN	TW
Total Sellers in MKT	30	45	46	34	53
...Market Selected	12	17	16	27	22
...Market Rejected	18	28	30	7	31
Women Clothes	10	14	17	11	17
...Market Selected	5	10	7	8	9
Women Shoes	1	4	5	2	4
...Market Selected	0	2	3	2	2
Women Bags	3	3	2	2	5
...Market Selected	2	0	1	1	1
Men Clothes	3	8	6	4	12
...Market Selected	1	4	1	2	5
Men Shoes	2	1	1	3	2
...Market Selected	2	0	0	3	1
Men Bags	1	0	1	0	0
...Market Selected	0	0	0	0	0
Baby & Kids Fashion	2	3	4	4	2
...Market Selected	2	1	2	4	0
Fashion Accessories	6	10	7	6	5
...Market Selected	0	0	1	5	4
Watches	0	0	0	0	0
...Market Selected	0	0	0	0	0
Sports & Outdoors	2	2	3	2	6
...Market Selected	0	0	1	2	0

Sellers that have existing presence in mkt

6

[Backup: Not existing in mkt TB sellers on SHP Pitching]: Markets selection rate ranges from 26% to 82% to provide incentives for pitching to acquire onto respective markets

Status	SG	MY	TH	VN	TW
Total Sellers in MKT	61	46	45	57	38
...Market Selected	33	22	37	31	10
...Market Rejected	28	24	8	26	28
Women Clothes	22	20	18	22	14
...Market Selected	14	10	16	16	5
Women Shoes	1	1	0	0	2
...Market Selected	1	1	0	0	0
Women Bags	3	3	3	4	2
...Market Selected	3	2	3	1	0
Men Clothes	14	10	9	13	6
...Market Selected	11	7	5	5	3
Men Shoes	1	0	1	0	1
...Market Selected	1	0	1	0	0
Men Bags	0	1	0	1	0
...Market Selected	0	0	0	0	0
Baby & Kids Fashion	8	3	4	5	5
...Market Selected	1	2	4	3	1
Fashion Accessories	9	6	8	10	8
...Market Selected	0	0	6	5	1
Sports & Outdoors	3	2	2	2	0
...Market Selected	2	0	2	1	0

Sellers that do not have presence in mkt

Furniture Update

[Furniture Progress: SG/MY] This week, we continued pushing to ramp up seller investment in MY and confirmed that our top GGP 润泽优 will source for all remaining 20k+ SKUs

Completed | In progress | Planned, to start | Delayed

Market	Topic	#	Task	PIC	Status
Phase 1 [Migration] - Cross-migrate existing TB SKUs on Shopee platform to SG and MY					
SG	Commercial	1	Align potential migration pool	Tina	Completed
		2	Align migration incentive plan to seller and marketing resource support to migrated SKUs	Tina	Completed
		3	Align SKU migration target and ADO target	Tina/Peggy	Completed
		4	Conduct seller pitching	Peggy	Completed
		5	Support seller onboarding / SKU listing	Peggy	In Progress
		6	Conduct marketing push	Tina	In Progress
	Service	7	Assess logistics blockers (channel availability and limits; rate card competitiveness; installation services)	Nicholas	Completed
		8	Launch installation service	Nicholas	In Progress
		9	Assess SLS Sea Shipping rates vs seller own vendors rates	Nicholas	Completed
		10	Lower SLS Sea Shipping rates	Felicity	Paused
MY	Commercial	11	Align potential migration pool	TM	Completed
		12	Align migration incentive plan to seller and marketing resource support to migrated SKUs	TM	Completed
		13	Align SKU migration target and ADO target	TM/Peggy	Completed
		14	Conduct seller pitching	Peggy	Completed
		15	Support seller onboarding / SKU listing	Peggy	In Progress
		16	Conduct marketing push	TM	In Progress
		17	Align migration incentive plan for CNLS sellers	TM	Completed
		18	Conduct seller pitching for CNLS sellers	Peggy	Completed
		19	Support SKU listing for CNLS sellers	Peggy	To start
		20	Conduct marketing push for CNLS sellers	TM	To start

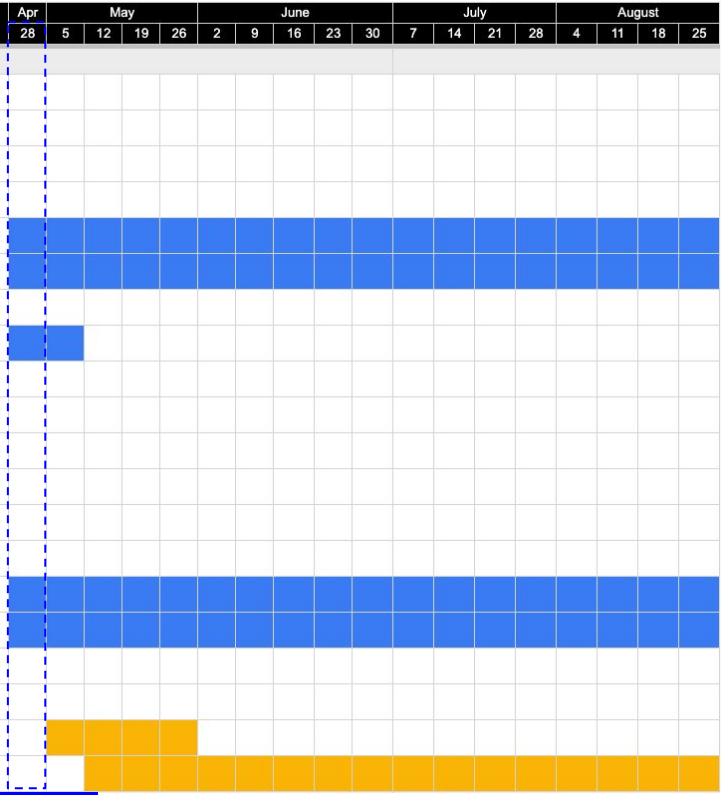

We are here

Highlights

- **Continued pushing for more seller investment in ads + vouchers for MY:** Current ads/vouchers usage for top sellers at 48% and 22% respectively; to ramp up coverage
- **Sourcing for MY to expand to 23k SKUs:** Following up from last week's update, our top SG GGP 润泽优 will source for all of MY's wishlist SKUs by June'25

[Furniture Progress: TH/VN] Migration is in progress for TH; 19/24 VN CNLS shops pitched successfully to join program but only 8 selected for trial push

Completed | In progress | Planned, to start | Delayed

Market	Topic	#	Task	PIC	Status
Phase 2 [Migration] - Cross-migrate existing TB SKUs on Shopee platform to PH/TH/VN/TW					
TH	Commercial	26	Align potential migration pool	Jan	Completed
		27	Align migration incentive plan to seller and marketing resource support to migrated SKUs	Jan	Completed
		28	Align SKU migration target and ADO target	Jan/Peggy	Delayed
		29	Conduct seller pitching	Peggy	Completed
		30	Support seller onboarding / SKU listing	Peggy	In Progress
		31	Conduct marketing push	Jan	To start
	Service	32	Understand current status of seaship/bulky channels in market	Lucas	Completed
		33	Assess logistics blockers (channel availability and limits; rate card competitiveness; installation services)	Nicholas	Completed
		34	(If applicable) Formulate logistics solution (e.g., new channel, higher limit and better price with vendor nego)	Lucas	In Progress
		35	(If applicable) Push sellers to adopt the new logistics solutions	Nicholas	To start
VN	Commercial	36	Align potential migration pool	Eric	Completed
		37	Align migration incentive plan to seller and marketing resource support to migrated SKUs	Eric	Completed
		38	Align SKU migration target and ADO target	Eric/Peggy	Delayed
		39	Conduct seller pitching	Peggy	Completed
		40	Support seller onboarding / SKU listing	Peggy	Paused
		41	Conduct marketing push	Eric	Paused
		42	Align migration incentive plan for CNLS sellers	Eric	Completed
		43	Conduct seller pitching for CNLS sellers	Peggy	Completed
		44	Support SKU listing for CNLS sellers	Peggy	In Progress
		45	Conduct marketing push for CNLS sellers	Eric	To start
	Service	46	Understand current status of seaship/bulky channels in market	Lucas	Paused
		47	Assess logistics blockers (channel availability and limits; rate card competitiveness; installation services)	Nicholas	Paused
		48	(If applicable) Formulate logistics solution (e.g., new channel, higher limit and better price with vendor nego)	Lucas	Paused
		49	(If applicable) Push sellers to adopt the new logistics solutions	Peggy	Paused

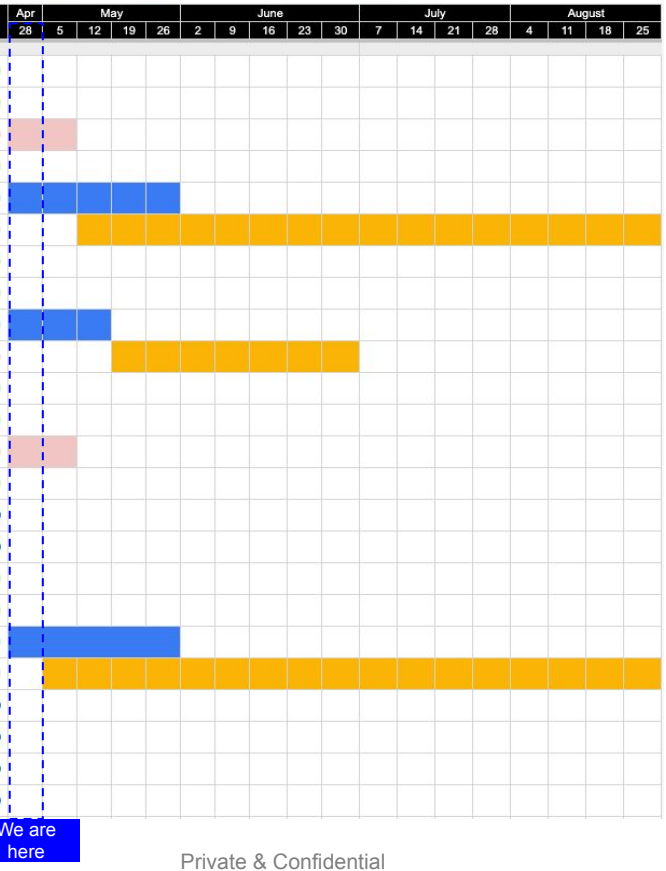

Highlights

TH Pitching Progress

- Migration in progress (200+ SKUs) by end May
- Marketing push to start from 12 May

VN Pitching Progress

- Following up from last week, pitching completed for 43 sellers. No sellers accepted to join CB, thus we will focus on CNLS
- For CNLS, 19/24 shops accepted to join program; but we will only focus on 8 to push for trial first due to budget constraints

[Furniture Performance] Reg MTD ADO 2.8k (-4.2% MoM; %CB -1.6%); ADG $134k (-11.1% MoM); SKU# 212k (+9.9% MoM)

Table: Overall regional performance for 48 TB sellers in the program (Apr full month)

			All Markets	SG	MY	PH	TH	VN
ADO	MTD		**2,792**	585	703	693	779	33
	M-1		**2,914**	691	710	679	767	67
	MoM	1	**-4.2%**	-15.4%	-0.9%	2.1%	1.5%	-50.5%
	CB% MTD		**18.4%**	25.3%	18.5%	13.3%	30.3%	2.6%
	CB% MoM		**-1.6%**	-1.3%	-1.1%	-3.2%	-0.2%	-1.7%
ADG	MTD		**$134,258**	$39,339	$25,791	$40,651	$25,943	$2,533
	MoM	2	**-11.1%**	-21.8%	-10.2%	-3.4%	3.9%	-48.6%
	CB% MTD		**38.5%**	45.0%	28.9%	39.2%	48.0%	17.9%
	CB% MoM		**-2.9%**	-2.5%	-3.1%	-6.8%	2.1%	-7.4%
ABS	MTD		**$48**	$67	$37	$59	$33	$77
	MoM		**-7.2%**	-7.6%	-9.4%	-5.4%	2.4%	3.8%
PC2 %	MTD		**6.9%**	8.4%	8.3%	4.6%	7.4%	2.4%
	MoM	3	**0.70%**	1.70%	1.00%	0.70%	-0.80%	-2.20%
	CB PC2		**6.1%**	9.8%	6.6%	5.0%	6.0%	3.1%
	Delta	3	**0.8%**	-1.4%	1.7%	-0.4%	1.4%	-0.7%
# SKUs	MTD		**212,511**	135,809	66,887	2,608	6,851	114
	MoM	4	**9.9%**	5.2%	18.8%	7.3%	35.7%	-64.2%
SKU effi	MTD		**1.31%**	0.43%	1.05%	26.57%	11.37%	28.95%
	M-1		**1.51%**	0.54%	1.26%	27.92%	15.20%	20.97%
	MoM		**-12.8%**	-19.5%	-16.6%	-4.8%	-25.2%	38.0%

Highlights

1. Reg MTD ADO 2.8k (-4.2% MoM); ADO as % CB -1.6% MoM
   - SG/MY stagnate/drop due to low seller investment committed (to push ads + vouchers for all top shops)
   - VN, drop is due to top GGP 中南 converting from CB to CNLS
2. Reg MTD ADG $134k (-11% MoM); ADG as %CB -2.9% MoM
3. PC2 6.9% (+0.7% MoM); +0.8% vs CB furniture PC2% - Similar to fashion, local's PC2 plan did not (re-working with SG/MY mkts to be more aggressive in their push e.g. co-sponsor vouchers)
4. SKU # 212k (+9.9% MoM); SKU# healthy across all mkts except VN drop due to top GGP exiting CB (explained in point #1)

[Furniture] Summary of focus initiatives (key changes from last update in blue)

Domain	#	Initiative	Market	Status	ETA
Grow SKU count	1	**Cross-market SKU migration**	SG/MY/TH	• For SG/MY, 82k SKUs added to local mkts since start of migration (SG RR 106%, MY RR 100%). 22k more SKUs to be added by end Jun • For TH, target to migrate 200 SKUs by end May	Ongoing till EOY
	2	**Acquire TB sellers (top + non-top)**	SG/MY	• Top 500 TB Furniture sellers: 9 sellers acquired in total (5 already in program, 3 to be added in May, 1 TBC) • Non-top TB 500: 2 seller acquired in total	May
	3	**SKU Sourcing**	SG/MY	• SG/MY: Sourced SKUs overall performance low. Next steps: ○ 1) SG increase exposure for top SKUs through microsites and DD participation 2) MY targets increased to source 23k SKUs; To be sourced by end June by top GGP	May-Jun
	4	**CNLS**	VN/MY	• VN pitching completed with 19/24 shops accepted but trial to only start on 8 shops first; MY only 2 shops (out of 86 accepted) due to unattractive package but these sellers will not be repitched	Start of VN trial: 6 May Deep-dive
Improve Logistics	5	**Set-up installation**	SG	• STO installation was planned for local only, will leverage local implementation to CB and launch Best installation ○ Local checking on target SKU list; Installation to launch in mid May	Mid-May
	6	**拆包 request**	SG/MY	• Due to furniture sellers items being too bulky, they need to split their parcels e.g. one sofa split into 3-4 parcels • Workaround solution: Use add-on gifts to allow sellers to split the parcels • Workaround solution facing ops issue causing seller penalty points; working with BPM on mid-long term solution request to be raised with same biz impact provided, with further push from JH as high priority	Early-May
	7	**Set-up bulky channel**	TH/PH/TW	• Strict dimension/weight limit for existing channel, restricting shipment of bulky parcels • TH/PH/TW: SLS on vendor negotiation and rate card	end-May (TH) end-Jun (PH/TW)

4 [CNLS MY/VN] MY low acceptance rate (2/86 shops) due to unattractive package - will not repitch; for VN, 19/24 shops accepted and will push 8 shops first due to budget constraints

Table: MY/VN CNLS Pitching Results

Reasons	MY				VN			
	Shop #	Shop %	ADO	ADO %	Shop #	Shop %	ADO	ADO %
Pitched	86	100%	5,159	100%	24	100%	3,209	100%
... Accepted	2	2%	14	0%	19	79%	2,865	89%
... Rejected	67	78%	4,665	90%	5	21%	344	11%
... Pending	17	20%	480	9%	0	0%	0	0%

Highlights:

- **[MY]:** Low acceptance rate (2%) due to unattractive seller commitment CNLS package; to complete pitching by next week. For remaining sellers, will not repitch as aligned with MY Local team
- **[VN]:** 19/24 shops accepted to join TB program; 8 selected for pilot test push (53% of total ADO) due to budget limitations
- **[SG]:** To explore CNLS for the top 2 sellers 中南万象 and 舰长 to join TB program after MY pitching concludes

[Backup - VN CNLS Package] Trial to run in May for 8 shops (shown in previous slide) using package shown below before deciding whether to ramp up to more shops

Table: VN Incentive Package (trial for May) offered to 8 shops

Marketing Package	Seller Commitment	Shopee Commitment
SKU Listing	List 10 new furniture SKUS in May	-
Paid Ads	Expense 1,500 USD in paid ads	-
Vouchers	-	15% off min spend 400k VND, cap 120k VND Cap at 500 USD (13 mil VND) per shop

F&B Update

[F&B Progress: SG/MY] 112 existing TB SHP sellers identified to start migration push; to also kickstart sourcing/acquisition in 1-2 weeks after incentive packages and targets aligned

Completed | In progress | Planned, to start | Delayed

Market	Topic	Sub-topic	#	Task	PIC	Status
Overall planning	Project Kickstart	Identify sellers	1	Identify TB sellers existing on SHP by CN SMT	Jolene	Completed
			2	Identify SHP sellers with TB SKUs by crawling top TB	Keith	Completed
		Estimate	3	Estimate overall migration potential and ADO potential	Nicholas	In Progress
SG	Commercial	Migration	4	Align potential migration pool	SG PIC (TBC)	In Progress
			5	Align migration incentive plan to seller and marketing	SG PIC (TBC)	In Progress
			6	Align SKUs migration target and ADO target	SG PIC/Jolene	In Progress
			7	Conduct seller pitching	Jolene	To start
			8	Support seller onboarding / SKU listing	Jolene	To start
			9	Conduct marketing push	SG PIC (TBC)	To start
		Crawling	10	Crawl TB Top SKUs	Keith	Completed
			11	Mapping to existing SHP SKUs	Keith	Completed
		Sourcing	12	Curate regional sourcing wishlist	Jason	Completed
			13	SCS/Lovito/CN Sellers/SIP to source	Max/Nicholas	In Progress
			14	Marketing resource alignment	Max	In Progress
			15	SKUs review	SG PIC (TBC)	To start
			16	Marketing push	SG PIC (TBC)	To start
		Acquisition	17	Identify TB Top 200 sellers	Keith	Completed
			18	Marketing resource alignment	Max	In Progress
			19	Conduct seller pitching	Jolene	To start
			20	Seller onboarding and SKU listing/migration	Jolene	To start
			21	Marketing push	SG PIC (TBC)	To start
		Crawled Matched SKUs Push	22	Selection of SKUs	SG PIC (TBC)	To start
			23	Marketing resource alignment	Max	To start
			24	SKUs migration	Jolene	To start
			25	Marketing push	SG PIC (TBC)	To start
MY	Commercial	Migration	26	Align potential migration pool	MY PIC (TBC)	In Progress
			27	Align migration incentive plan to seller and marketing	MY PIC (TBC)	In Progress
			28	Align SKUs migration target and ADO target	MY PIC/Jolene	In Progress
			29	Conduct seller pitching	Jolene	To start
			30	Support seller onboarding / SKU listing	Jolene	To start
			31	Conduct marketing push	MY PIC (TBC)	To start
		Crawling	32	Crawl TB Top SKUs	Keith	Completed
			33	Mapping to existing SHP SKUs	Keith	Completed
		Sourcing	34	Curate regional sourcing wishlist	Jason	Completed
			35	SCS/Lovito/CN Sellers/SIP to source	Max/Nicholas	In Progress
			36	Marketing resource alignment	Max	In Progress
			37	SKUs review	MY PIC (TBC)	To start
			38	Marketing push	MY PIC (TBC)	To start
		Acquisition	39	Identify TB Top 200 sellers	Keith	Completed
			40	Marketing resource alignment	Max	In Progress
			41	Conduct seller pitching	Jolene	To start
			42	Seller onboarding and SKU listing/migration	Jolene	To start
			43	Marketing push	MY PIC (TBC)	To start
		Crawled Matched SKUs Push	44	Selection of SKUs	MY PIC (TBC)	To start
			45	Marketing resource alignment	Max	To start
			46	SKUs migration	Jolene	To start
			47	Marketing push	MY PIC (TBC)	To start

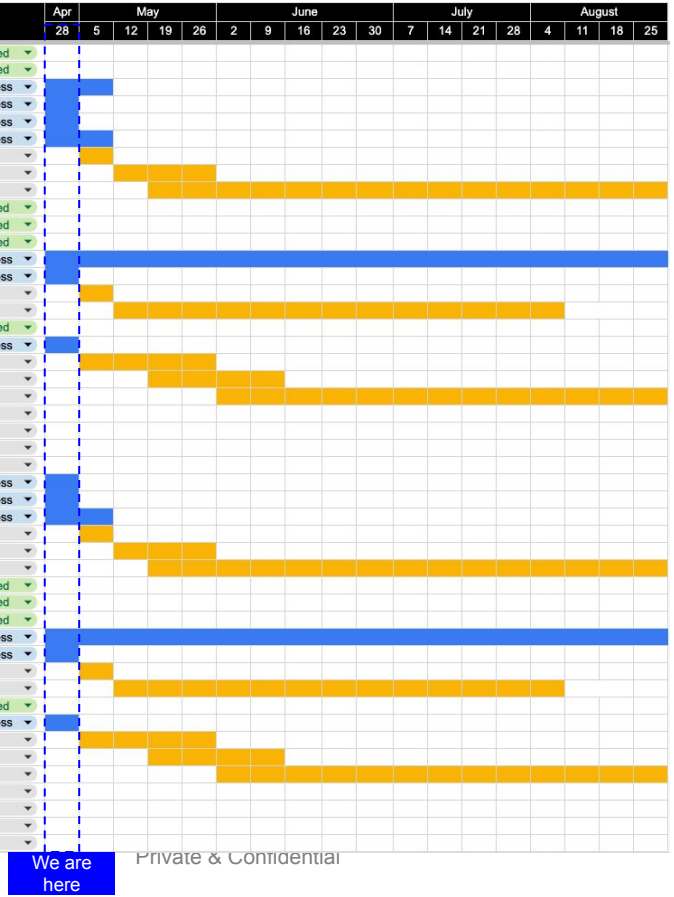

Highlights (changes from last week highlighted in blue)

SG/MY to kick start first

- **Existing SHP TB sellers:** Identified **112 TB sellers on SHP** to start push (+ migration) from 12 May
- **Incentive Package Alignment:** To get packages for migration, acquisition, sourcing by start of next week
- **Acquisition:** Identified list of 200 top TB sellers to acquire; to start end next week after package confirmed and CN back from holiday
- **Sourcing:** Target alignment with CN complete; sourcing to start from mid next week after CN back from holiday

TH to start after all SG/MY initiatives kick-started

Private & Confidential
