Counter Taobao Weekly Update

Week ending 20 June 2025

Fashion Update

[Fashion progress: new top TB seller acquisition] 24 new sellers acquired in Jun (+3 since last weekly update); YTD 26 to 44 shops opened in respective markets, generating 1.4k ADO

Completed | In progress | To start | Delayed

Market	Topic	#	Task	PIC	Status
Acquire top TB sellers / SKUs that are not on SHP					
		42	Sellers review	Tina	Completed
		43	Marketing resource alignment	Tina	Completed
		44	Conduct seller pitching	Lynn	In Progress
		45	Seller onboarding and SKU listing/migration	Lynn	In Progress
SG	Commercial	46	Marketing push	Tina	In Progress
		47	Sellers review	Max	Completed
		48	Marketing resource alignment	Max	Completed
		49	Conduct seller pitching	Lynn	In Progress
		50	Seller onboarding and SKU listing/migration	Lynn	In Progress
MY	Commercial	51	Marketing push	Max	In Progress
		52	Sellers review	Tiffany	Completed
		53	Marketing resource alignment	Tiffany	Paused
		54	Conduct seller pitching	Lynn	In Progress
		55	Seller onboarding and SKU listing/migration	Lynn	In Progress
TH	Commercial	56	Marketing push	Tiffany	In Progress
		57	Sellers review	Eric	Completed
		58	Marketing resource alignment	Eric	Completed
		59	Conduct seller pitching	Lynn	In Progress
		60	Seller onboarding and SKU listing/migration	Lynn	In Progress
VN	Commercial	61	Marketing push	Eric	In Progress
		62	Sellers review	Amanda	Completed
		63	Marketing resource alignment	Amanda	Completed
		64	Conduct seller pitching	Lynn	In Progress
		65	Seller onboarding and SKU listing/migration	Lynn	In Progress
TW	Commercial	66	Marketing push	Amanda	In Progress
		67	Sellers review	Ashley	Completed
		68	Marketing resource alignment	Ashley	Completed
		69	Conduct seller pitching	Lynn	In Progress
		70	Seller onboarding and SKU listing/migration	Lynn	To start
PH	Commercial	71	Marketing push	Ashley	To start

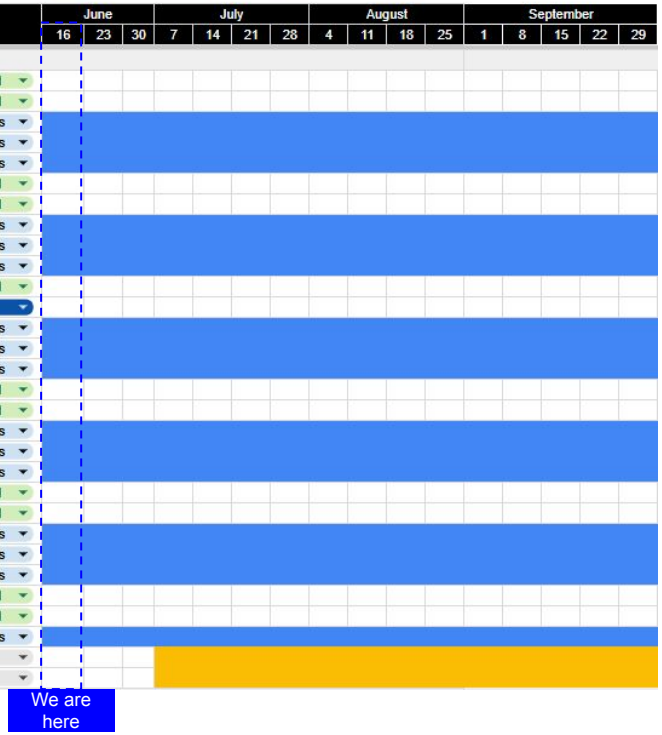

Highlights

[VN, TH, TW, SG, MY]

- In June, 24 sellers (+3 from last update) were newly acquired.
- From Mar-May batches, 26 to 44 shops opened across all markets and added into tracking, generating 1.4k ADO (~5% of program)
- CNSIP Batch 5 (from Mar/Apr batch and remaining of universe pool not in program): All 587 shops added in program from 14 Jun
- Target re-alignment for all categories and markets (part of CN x Reg effort) - to be completed by this week

[Fashion progress: sourcing] Sourcing began on 10 Jun across all markets with 150-1k SKUs sourced across markets to start marketing push in Jul; working with CN team on how to improve the quantity sourced

Completed | In progress | To start | Delayed

Market	Topic	#	Task	PIC	Status
Crawl and source top TB SKUs unmatched on SHP					
SG	Commercial	72	Crawl TB SKUs	Keith	Completed
		73	Mapping to existing SHP SKUs	Keith	Completed
		74	Marketing resource alignment	Tina	Completed
		75	SOP Alignment	Nicholas/Lynn	Completed
		76	Sourcing of SKUs	SCS/Lynn	In Progress
		77	Marketing push	Tina	To start
MY	Commercial	78	Crawl TB SKUs	Keith	Completed
		79	Mapping to existing SHP SKUs	Keith	Completed
		80	Marketing resource alignment	Max	Completed
		81	SOP Alignment	Nicholas/Lynn	Completed
		82	Sourcing of SKUs	SCS/Lynn	In Progress
		83	Marketing push	Max	To start
TH	Commercial	84	Crawl TB SKUs	Keith	Completed
		85	Mapping to existing SHP SKUs	Keith	Completed
		86	Marketing resource alignment	Tiffany	Completed
		87	SOP Alignment	Nicholas/Lynn	Completed
		88	Sourcing of SKUs	SCS/Lynn	In Progress
		89	Marketing push	Tiffany	To start
VN	Commercial	90	Crawl TB SKUs	Keith	Completed
		91	Mapping to existing SHP SKUs	Keith	Completed
		92	Marketing resource alignment	Eric	Completed
		93	SOP Alignment	Nicholas/Lynn	Completed
		94	Sourcing of SKUs	SCS/Lynn	In Progress
		95	Marketing push	Eric	To start
TW	Commercial	96	Crawl TB SKUs	Keith	Completed
		97	Mapping to existing SHP SKUs	Keith	Completed
		98	Marketing resource alignment	Amanda	Paused
		99	Sourcing of SKUs	SCS/Lynn	Paused
		100	Marketing push	Amanda	Paused
PH	Commercial	101	Crawl TB SKUs	Keith	Completed
		102	Mapping to existing SHP SKUs	Keith	Completed
		103	Marketing resource alignment	Ashley	Completed
		104	SOP Alignment	Nicholas/Lynn	Completed
		105	Sourcing of SKUs	SCS/Lynn	In Progress
		106	Marketing push	Ashley	To start

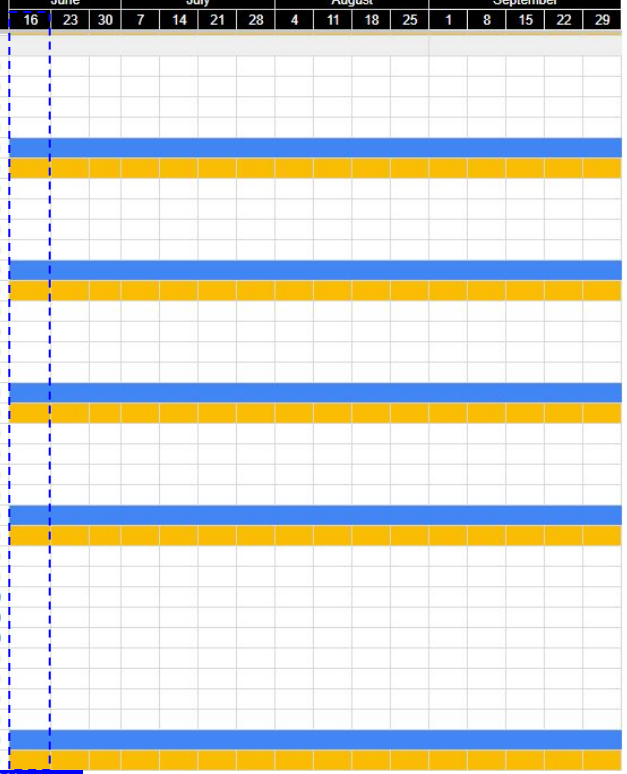

Highlights

- **Pitching for sourcing started on 10 June for all markets**: Sharing results with markets for review; review results to be in on 25 Jun
- **# SKUs sourced (new to SHP):** 150 (SG), 222 (MY), 1,022 (TH), 685 (VN), 246 (PH). Push to start in July

[Fashion performance] ADO 43.8k (MoM +21% %CB +0.6pp); ADG $468k (MoM +23%, %CB +1.5pp); SKU# 688k (MoM -0.3%)

Table: Fashion Performance (1-18 Jun)

		All Markets	SG	MY	TW	PH	TH	VN
ADO	MTD	**43,784**	638	4,650	464	18,479	9,966	9,587
	M-1	**36,118**	696	4,280	416	13,633	9,150	7,942
	MoM	1 **21.2%**	-8.3%	8.6%	11.4%	35.5%	8.9%	20.7%
	WTD	**46,774**	686	5,688	460	18,020	10,821	11,100
	WoW	**22.4%**	30.2%	30.5%	3.2%	9.6%	28.3%	38.8%
	CB% MTD	5.4%	1.8%	3.9%	2.3%	7.5%	8.7%	3.5%
	CB% M-1	4.8%	2.0%	3.8%	2.0%	5.8%	8.0%	3.3%
	CB% MoM	**0.6%**	-0.2%	0.0%	0.3%	1.7%	0.8%	0.2%
ADG	MTD	**$468,320**	$11,751	$51,021	$11,228	$183,128	$128,296	$82,896
	M-1	**$382,176**	$11,074	$50,825	$9,188	$147,860	$94,642	$68,587
	MoM	2 **22.5%**	6.1%	0.4%	22.2%	23.9%	35.6%	20.9%
	CB% MTD	**9.9%**	3.0%	5.6%	2.2%	14.7%	16.7%	9.0%
	CB% M-1	**8.4%**	2.9%	5.4%	1.9%	12.6%	13.3%	8.0%
	CB% MoM	**1.5%**	0.1%	0.2%	0.3%	2.1%	3.4%	1.1%
ABS	MTD	**$11**	$18	$11	$24	$10	$13	$9
	MoM	**1.1%**	15.7%	-7.6%	9.7%	-8.6%	24.5%	0.1%
PC2	MTD	**-$7,767**	$877	-$683	$1,102	-$7,256	-$2,455	$648
	MoM	**-$14,278**	$355	-$2,259	$120	-$6,819	-$4,241	-$1,434
PC2 %	MTD	**-1.7%**	7.8%	-1.4%	9.9%	-4.0%	-1.9%	0.8%
	MoM	**-3.4%**	2.9%	-4.5%	-0.8%	-3.7%	-3.8%	-2.3%
	CB PC2	-0.8%	10.1%	-0.1%	7.6%	-2.8%	-2.9%	-7.5%
	Delta	**-0.9%**	**-2.2%**	**-1.3%**	**2.3%**	**-1.2%**	**1.0%**	**8.3%**
# SKUs	MTD	**687,863**	76,420	90,748	69,594	170,482	135,821	144,799
	MoM	3 **-0.3%**	-4.0%	2.0%	-4.4%	0.1%	-1.7%	3.4%
	WTD	708,633	82,584	94,130	71,196	169,677	139,565	151,483
	WoW	**3.5%**	**9.1%**	**4.4%**	**5.0%**	**-0.5%**	**3.1%**	**4.4%**
SKU effi	MTD	**6.37%**	0.83%	5.12%	0.67%	10.84%	7.34%	6.62%
	MoM	**21.6%**	-4.4%	6.5%	16.6%	35.4%	10.8%	16.8%

Highlights

1. Reg ADO 43.8k (+21% MoM) due to strong push by PH + VN
   - SG 638 ADO (-58 ADO): Fall largely due to CNSIP seller 永嘉恒歌纺织绣品 -53 ADO being (1) penalized for fulfilment issues till July 6th and hence (2) cannot participate in campaigns
   - PH 18.5k ADO (+35% MoM): growth due to push of sports and outdoors apparels
   - VN: 9.6k (+20% MoM); growth due to PRM push by platform and increased seller investment
2. Reg ADG $468k (+23% MoM); %CB 1.5pp grew across all markets. Outperforming CB in terms of ABS
3. Reg SKU# 688k (-0.3% MoM), overall SKU# stable, SG SKU 76k (-4%) and TW SKU 70k (-4.4%) mainly due to delisting of OOS/out-of-season SKUs

[Fashion] Overview of initiatives: 24 sellers acquired in June (total of 95 thus far); June sourcing added 0.15k-1k new to SHP SKUs per market; ERP trial ongoing and will ramp up in Jul

Domain	#	Initiative	Market	Status
Grow SKU count	1	Cross-market SKU migration/new upload	All (except PH)	299.5k new SKUs added since program start; Jun MTD SKU# Overall RR: SG: 105%, MY: 127%, TH: 109%, VN: 129%, TW: 122%
	2	TB seller acquisition (manual pitching)	All	• Jun: 24 newly acquired sellers (+3 from batch 2 of Jun), mkts selected 19-21 sellers of batch 1, pending mkts review on the newly added 3 sellers [ETA: 20 Jun] • Mar-May: 26 to 44 sellers opened shops across the markets, generating 1.4k ADO with 30k SKUs
	3	TB seller acquisition (ERP)	All	• Trial with select sellers ongoing currently; no system issues thus far (102 orders generated till date) • CN pitching to more sellers to join the trial in June; and ramp-up via mass pitching to start in Jul
	4	Crawling from LZD/TB	SG/MY/VN/TH/TW/PH	[Completed] All mkts: Recrawl from TB (instead of LZD) to improve matching and sourcing wishlist quality completed, shared with all markets
	5	SKU Sourcing	SG/MY/VN/TH/PH	Sourcing started for all markets except for TW (will not proactively take part in sourcing) • Started on 10 June, pitching results in and shared to markets for review by 25 Jun • New to SHP SKU# sourced: 150 (SG), 222 (MY), 1,022 (TH), 685 (VN), 246 (PH); working with CN to improve this further • SCS sourcing will start officially in Aug due to greater constraints and different focus categories
	6	TB seller self-nomination	SG/MY/VN/TH/TW	[Completed] Total of 78 sellers identified, 12-27 sellers existing in markets are added into program. • [Sellers not in market] Accepted sellers opened shop and added into hit list from 1st Jun • [Rejected/Not selected sellers]: Shops opened, sale started from 11 Jun

Furniture Update

[Furniture progress: SG/MY] MY CNLS successfully pitched to 51 shops, added into program for tracking and incentives to start from 1 Jul; SG secured top GGPs 中南 and 舰长 agreement, to finalize shops by next week

Completed | In progress | Planned, to start | Delayed

Market	Topic	#	Task	PIC	Status
Phase 1 [Migration] - Cross-migrate existing TB SKUs on Shopee platform to SG and MY					
SG	Commercial	1	Align potential migration pool	Tina	Completed
		2	Align migration incentive plan to seller and marketing resource support to migrated SKUs	Tina	Completed
		3	Align SKU migration target and ADO target	Tina/Peggy	Completed
		4	Conduct seller pitching	Peggy	Completed
		5	Support seller onboarding / SKU listing	Peggy	In Progress
		6	Conduct marketing push	Tina	In Progress
		7	Align migration incentive plan for CNLS sellers	Tina	Completed
		8	Conduct seller pitching for CNLS sellers	Peggy	In Progress
		9	Support SKU listing for CNLS sellers	Peggy	To start
		10	Conduct marketing push for CNLS sellers	Tina	To start
	Service	11	Assess logistics blockers (channel availability and limits; rate card competitiveness; installation services)	Nicholas	Completed
		12	Launch installation service	Nicholas	Delayed
		13	Assess SLS Sea Shipping rates vs seller own vendors rates	Nicholas	Completed
		14	Lower SLS Sea Shipping rates	Felicity	Paused
MY	Commercial	15	Align potential migration pool	TM	Completed
		16	Align migration incentive plan to seller and marketing resource support to migrated SKUs	TM	Completed
		17	Align SKU migration target and ADO target	TM/Peggy	Completed
		18	Conduct seller pitching	Peggy	Completed
		19	Support seller onboarding / SKU listing	Peggy	In Progress
		20	Conduct marketing push	TM	In Progress
		21	Align migration incentive plan for CNLS sellers	TM	Completed
		22	Conduct seller pitching for CNLS sellers	Peggy	Completed
		23	Support SKU listing for CNLS sellers	Peggy	In Progress
		24	Conduct marketing push for CNLS sellers	TM	In Progress

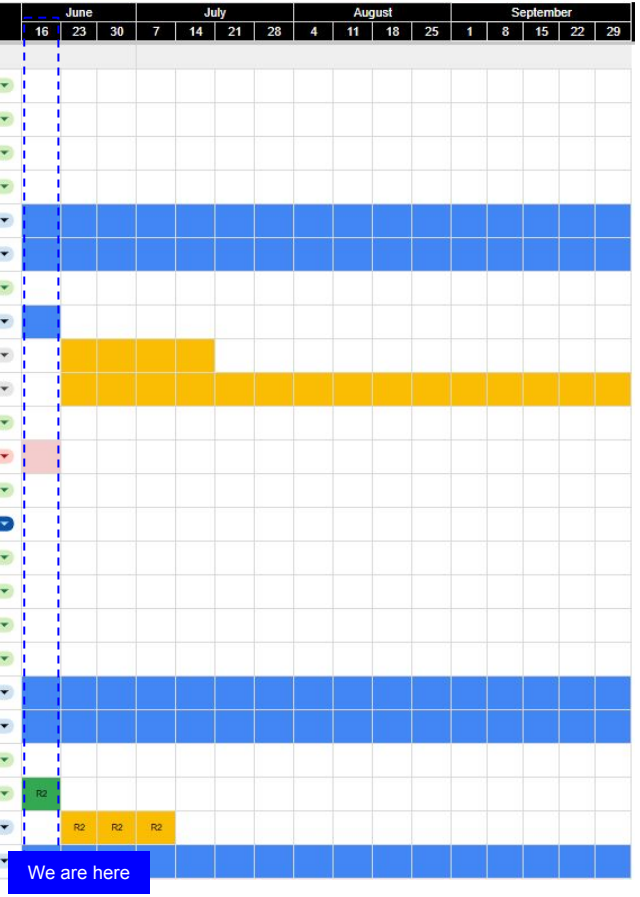

Highlights

- **Sourcing for MY by top GGP:** Sourced 12.3k SKUs in Jun, meeting overall 23k SKU # target by Jun; passed to markets for marketing push starting from 27 Jun
- **SG CNLS:** 中南 and 舰长 both agreed to join with 10 shops each, in progress of confirming on the shops to join program [ETA: 26 Jun]. Push to start in Jul
- **MY CNLS:** Pitching completed with 51 sellers accepting to join program; Push to start in Jul

[Furniture Progress: TH/VN] Alignment on VN CNLS incentive and seller list ongoing, push to start in July

Completed | In progress | Planned, to start | Delayed

Market	Topic	#	Task	PIC	Status
Phase 2 [Migration] - Cross-migrate existing TB SKUs on Shopee platform to PH/TH/VN/TW					
TH	Commercial	25	Align potential migration pool	Jan	Completed
		26	Align migration incentive plan to seller and marketing resource support to migrated SKUs	Jan	Completed
		27	Align SKU migration target and ADO target	Jan/Peggy	Completed
		28	Conduct seller pitching	Peggy	Completed
		29	Support seller onboarding / SKU listing	Peggy	In Progress
		30	Conduct marketing push	Jan	In Progress
	Service	31	Understand current status of seaship/bulky channels in market	Lucas	Completed
		32	Assess logistics blockers (channel availability and limits; rate card competitiveness; installation services)	Nicholas	Completed
		33	(If applicable) Formulate logistics solution (e.g., new channel, higher limit and better price with vendor nego)	Lucas	Completed
		34	(If applicable) Push sellers to adopt the new logistics solutions	Nicholas	In Progress
VN	Commercial	35	Align potential migration pool	Eric	Completed
		36	Align migration incentive plan to seller and marketing resource support to migrated SKUs	Eric	Completed
		37	Align SKU migration target and ADO target	Eric/Peggy	Completed
		38	Conduct seller pitching	Peggy	Completed
		39	Support seller onboarding / SKU listing	Peggy	Paused
		40	Conduct marketing push	Eric	Paused
		41	Align migration incentive plan for CNLS sellers	Eric	In Progress
		42	Conduct seller pitching for CNLS sellers	Peggy	To start
		43	Support SKU listing for CNLS sellers	Peggy	To start
		44	Conduct marketing push for CNLS sellers	Eric	To start
All	Commercial	49	Identify more TB SHP sellers via broadcasting	Peggy	In Progress
		50	Market review and selection of sellers	All	To start
		51	Conduct seller pitching	Peggy	In Progress
		52	Add successful sellers into existing pool	Peggy	To start

Highlights

TH Bulky Channel

- Channel official launch on 10 Jun with 240 sellers whitelisted on 13 Jun; pending tracker set up by 27 Jun to evaluate seller performance after transitioning to new bulky channel

VN CNLS

- Draft incentives shared, to align and confirm on incentives [ETA: 23 Jun]
- Pitching to begin once incentive and seller list is confirmed [Final Results ETA: 30 Jun]

[Furniture Performance] Reg ADO 3.3k (+15% MoM,); ADG $161k (+11% MoM); SKU# 279k (+16% MoM)

Table: Furniture Performance (Jun 1-18)

			All Markets	SG	MY	PH	TH	VN
ADO	MTD		**3,298**	573	503	964	1,219	39
	M-1		**2,859**	570	513	872	877	27
	MoM	1	**15.3%**	0.5%	-2.0%	10.6%	39.0%	41.9%
	WTD		**3,067**	566	533	948	978	42
	WoW		**10.8%**	9.2%	6.6%	17.6%	6.7%	51.7%
	CB% MTD		**19.4%**	24.2%	15.5%	15.0%	33.1%	3.0%
	CB% MoM		**1.0%**	-1.3%	-0.2%	-0.1%	3.9%	0.8%
ADG	MTD		**$161,190**	$39,900	$20,539	$60,974	$36,923	$2,853
	M-1		**$145,049**	$37,896	$22,210	$52,847	$29,814	$2,281
	MoM	2	**11.1%**	5.3%	-7.5%	15.4%	23.8%	25.1%
	CB% MTD		**40.5%**	46.1%	24.8%	44.2%	47.8%	21.1%
	CB% MoM		**1.7%**	0.6%	0.1%	1.0%	2.2%	3.3%
ABS	MTD		**$49**	$70	$41	$63	$30	$74
	MoM		**-3.7%**	4.8%	-5.6%	4.3%	-10.9%	-11.9%
PC2	MTD		**$9,507**	$5,383	$2,629	$686	$665	$59
	MoM		**$377**	$399	-$170	$130	$9	$6
PC2 %	MTD		**5.9%**	13.2%	12.7%	1.1%	1.8%	2.0%
	MoM		**-0.4%**	0.0%	0.1%	0.0%	-0.4%	-0.3%
	CB PC2		**6.3%**	11.7%	7.9%	3.8%	3.4%	1.0%
	Delta		**-0.4%**	1.5%	4.8%	-2.8%	-1.6%	1.0%
# SKUs	MTD		**278,830**	182,953	85,520	3,586	6,314	128
	MoM	3	**16.0%**	10.2%	34.3%	8.4%	-9.8%	8.1%
	WTD		**282,378**	182,663	89,833	3,609	5,675	135
	WoW		**-0.2%**	-1.2%	2.6%	0.5%	-9.5%	4.0%
SKU effi	MTD		**1.18%**	0.31%	0.59%	28.45%	19.71%	30.97%
	MoM		**-0.6%**	-8.8%	-27.0%	8.0%	57.3%	34.3%

Highlights

1. Reg MTD ADO 3.3k (+15% MoM), driven by TH push
   - TH ADO 1.2k (+39% MoM) due to increased seller investment and platform push as program started and is ramping up
   - MY decline due to 2 reasons updated last week (sellers moving to CNLS, and penalty points preventing sellers from participating in campaign). Will push sellers after points are cleared
2. Reg MTD ADG $161k (+11% MoM), mainly driven by strong ADO growth
3. SKU # 279k (+16% MoM); mainly driven by MY SKU# +34% MoM from 润泽优 relisting SKUs (from system bug)

[Furniture] Overview of initiatives: +23k new to MY SHP SKUs added, sourcing target complete this week; SG/MY/VN CNLS to start in July

Domain	#	Initiative	Market	Status
Grow SKU count	1	**Cross-market SKU migration**	SG/MY/TH	• 199k SKUs added to SG/MY/TH since the start of the program; MTD 685 ADO from new SKUs (20% of program ADO)
	2	**TB seller acquisition**	SG/MY	• Top 500 TB Furniture sellers: 12 sellers acquired in total (11 already in program, 1 to be added by end Jun) • Non-top TB 500: 7 sellers acquired in total (4 already in program, 3 to be added by end Jun)
	3	**TB seller self-nomination**	All	• 17 TB sellers identified, pitching to sellers to join program via migration/sourcing [ETA: 20 Jun] • Another 500 sellers identified do not have TB shops; pending CN team to review the list and shops assortment [ETA: 27 Jun]
	4	**SKU Sourcing**	SG/MY	• SG: Completed 6k sourcing SKU # target in Apr [Completed] • MY: 润泽优 (one of top GGPs) completed sourcing of 12.3k SKUs in Jun, achieving overall target of 23k
	5	**CNLS**	VN/MY/SG	• VN: Pending confirmation on incentives and seller list, to begin pitching after and conclude by 30 Jun • MY: Pitching completed with 51 sellers accepting to join program, incentives to begin 1 Jul • SG: 中南 and 舰长 both agreed to join with 10 shops each, in progress of confirming on the shops to join program [ETA: 26 Jun]
Improve Logistics	6	**Set-up installation**	SG	• STO installation was planned for local only • To replicate local channel design to CB and launch Best installation; 34 sellers added into seller whitelist with 42 SKUs tagged with installation, feature launched with greyscale started 20 Jun, open to 100% by 9 Jul
	7	**拆包 request**	SG/MY	• Issue: sellers need to split their bulky item parcels, e.g., one sofa split into 3-4 parcels; workaround solution facing ops issue causing seller penalty points • System solution: approved as P1, pipeline sequence confirmed, next steps for FPM to start on PRD [ETA: pending]
	8	**Set-up bulky channel**	TH/PH/TW	• TH: Channel officially went live on 10 June, currently 240 sellers whitelisted onto channel • TW: Channel trial to happen after code freeze period over on 24 June before official launch EOM • PH: To de-prioritize due to competitive shipping channel with TB (after TB removal of sea shipping channel)

F&B Update

[F&B Progress: Existing seller & Acquisition] 17 sellers accepted to join SG/MY program for migration, migration to complete by end-Jun; TH pending incentives confirmation before pitching starts by 24 Jun

Completed | In progress | Planned, to start | Delayed

Market	Topic	#	Task	PIC	Status
[Migration] - Cross-migrate existing TB SKUs on Shopee platform					
SG	Commercial	4	Align potential migration pool	Kaiwen	Completed
		5	Align migration incentive plan to seller and marketing	Kaiwen	Completed
		6	Align SKUs migration target and ADO target	Kaiwen/Jolene	Completed
		7	Conduct seller pitching	Jolene	Completed
		8	Support seller onboarding / SKU listing	Jolene	In Progress
		9	Conduct marketing push	Kaiwen	To start
MY	Commercial	10	Align potential migration pool	Kaiwen	Completed
		11	Align migration incentive plan to seller and marketing	Kaiwen	Completed
		12	Align SKUs migration target and ADO target	Kaiwen/Jolene	Completed
		13	Conduct seller pitching	Jolene	Completed
		14	Support seller onboarding / SKU listing	Jolene	In Progress
		15	Conduct marketing push	Kaiwen	To start
TH	Commercial	16	Align potential migration pool	Nut	Completed
		17	Align migration incentive plan to seller and marketing	Nut	Delayed
		18	Align SKUs migration target and ADO target	TH PIC/Jolene	Delayed
		19	Conduct seller pitching	Jolene	To start
		20	Support seller onboarding / SKU listing	Jolene	To start
		21	Conduct marketing push	Nut	To start
[Acquisition] - Acquire top TB sellers / SKUs that are not on SHP					
SG	Commercial	22	Identify TB Top 200 sellers	Keith	Completed
		23	Marketing resource alignment	Max	Completed
		24	Conduct seller pitching	Jolene	In Progress
		25	Seller onboarding and SKU listing/migration	Jolene	To start
		26	Marketing push	Kaiwen	To start
MY	Commercial	27	Identify TB Top 200 sellers	Keith	Completed
		28	Marketing resource alignment	Max	Completed
		29	Conduct seller pitching	Jolene	In Progress
		30	Seller onboarding and SKU listing/migration	Jolene	To start
		31	Marketing push	Kaiwen	To start
TH	Commercial	32	Identify TB Top 200 sellers	Keith	Completed
		33	Marketing resource alignment	Max	Delayed
		34	Conduct seller pitching	Jolene	In Progress
		35	Seller onboarding and SKU listing/migration	Jolene	To start
		36	Marketing push	Nut	To start

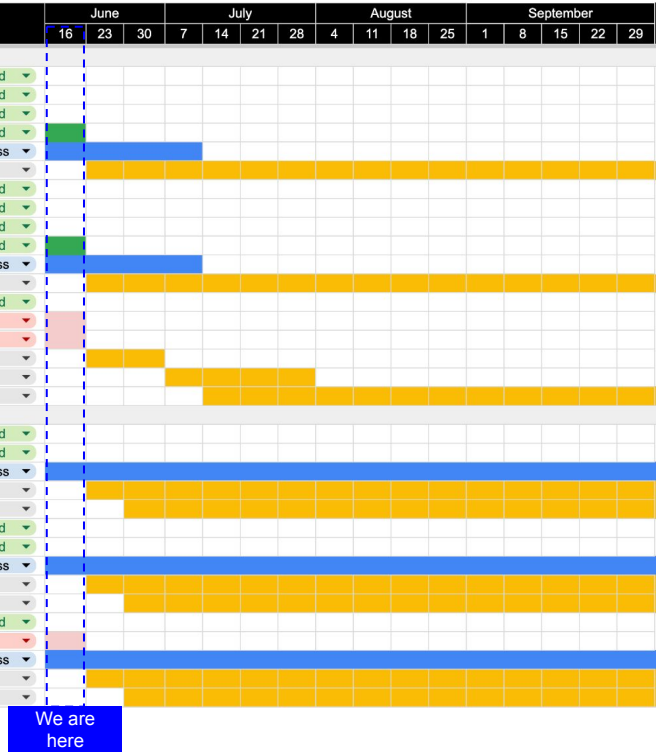

Highlights

- **Existing SHP TB sellers:** 32 TB sellers on SHP identified (after removing sellers that are uncontactable and selling a mix of categories)
  - SG/MY selected 31 sellers (97%); 16 and 17 sellers accepted to join program respectively. Migration in progress [ETA: end Jun]
  - TH selected 26 sellers (81%); pending incentives confirmation [ETA: 24 Jun]
- **Acquisition:**
  - Pitching for top 200 TB sellers have concluded with 12 sellers onboarded onto SHP
  - Next step: to pitch for them to join program [ETA: 25 Jun]

[F&B Progress: Sourcing] Pitching ongoing and to conclude by 25 Jun, adding +0.1-0.5k new to SHP SKUs per market; to push in Jul

Completed | In progress | Planned, to start | Delayed

Market	Topic	#	Task	PIC	Status
[Sourcing] - Crawl and match top TB SKUs on SHP; Source those unmatched on SHP					
SG	Commercial	37	Crawl TB Top SKUs	Keith	Completed
		38	Mapping to existing SHP SKUs	Keith	Completed
		39	Curate regional sourcing wishlist	Jason	Completed
		40	SCS/CN Sellers to source	Max/Nicholas	In Progress
		41	Marketing resource alignment	Max	Completed
		42	SKUs review	Kaiwen	To start
		43	Marketing push	Kaiwen	To start
MY	Commercial	44	Crawl TB Top SKUs	Keith	Completed
		45	Mapping to existing SHP SKUs	Keith	Completed
		46	Curate regional sourcing wishlist	Jason	Completed
		47	SCS/CN Sellers to source	Max/Nicholas	In Progress
		48	Marketing resource alignment	Max	Completed
		49	SKUs review	Kaiwen	To start
		50	Marketing push	Kaiwen	To start
TH	Commercial	51	Crawl TB Top SKUs	Keith	Completed
		52	Mapping to existing SHP SKUs	Keith	Completed
		53	Curate regional sourcing wishlist	Jason	Completed
		54	SCS/CN Sellers to source	Max/Nicholas	In Progress
		55	Marketing resource alignment	Max	Completed
		56	SKUs review	Nut	To start
		57	Marketing push	Nut	To start

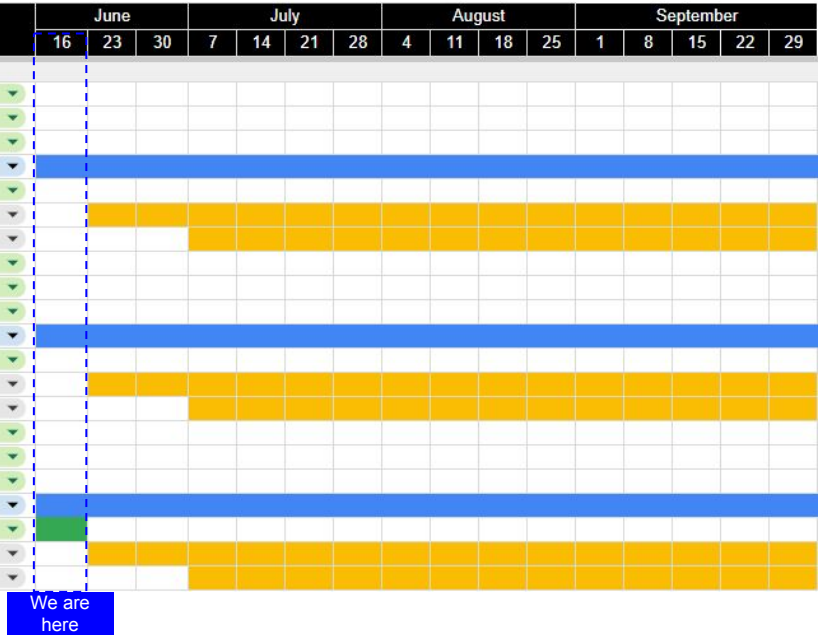

Highlights

- June current pitching results in as of 17 Jun - 524 (SG), 331 (MY), 16 (TH)
- Seller SKU nomination list clean-up in progress; to be shared to markets after clean up on 25 Jun and get markets to select by 30 Jun

[F&B] Overview of initiatives: 17 sellers agreed to join seller program and start migration for SG/MY; 12 sellers acquired out of top 200 sellers, to start push in July

Domain	#	Initiative	Market	Status
Grow SKU count through migration, acquisition, sourcing	1	Cross-market SKU migration	SG/MY/TH	• SG/MY: 16/31 and 17/31 sellers accepted to join program via migration/shop opening for SG and MY respectively; SKUs migration in progress [ETA: end Jun] • TH: Pending budget approval and incentive alignment ETA 24 Jun Deep-dive
	2	SKU Sourcing	SG/MY/TH	• SG/MY/TH: June current pitching results in (as of 17 Jun) - 524 (SG), 331 (MY), 16 (TH). To pass to markets for review by 30 Jun after clean up of seller SKU nomination list
	3	TB seller acquisition	SG/MY/TH	• SG/MY: Acquisition pitching for top 200 TB sellers concluded with 12 sellers onboarded onto SHP, to pitch for them to join program [ETA: 25 Jun] • TH: Pending incentive alignment ETA 24 Jun Deep-dive
	4	TB seller self-nomination	SG/MY/TH	• To start seller broadcasting on 11 Jun via 9 channels including CNSC banner, SEH announcement, social media, etc; First round of results by 20 Jun

[F&B Existing Sellers Pitching Progress] Out of 31 sellers, 16-17 sellers accepted to join program via migration/opening new shop in SG/MY; migration of SKUs started and to complete by end Jun

Table: F&B Existing Sellers Pitching Progress

	Status	SG			MY			Remarks
		Seller #	SKU #	ADO	Seller #	SKU #	ADO	
1	Pitching Pool	32	4,350	45	32	3,889	342	
	(1) Selected by market	**31**	**4,350**	**45**	**31**	**3,889**	**342**	
2	... Accepted	16	3,438	34	17	3,528	319	SKUs migration started this week, complete migration by end Jun
	... Pending to accept via migration tool	2	6	0	7	140	20	Invited to migrate via migration tool [ETA: 27 Jun]
	... In discussion	9	798	8	7	221	3	Did not reject explicitly, still in discussion [ETA: 23 Jun]
3	... Rejected, pitch CNSIP	4	108	2	0	0	0	
	(2) Not selected by market, pitch CNSIP	**1**	**0**	**0**	**1**	**0**	**0**	

Highlights

1. A total of 32 TB sellers from existing SHP pool are identified for pitching; with 4.3k and 3.9k SKUs and 45 and 341 ADO in SG/MY respectively
2. Of the 31 sellers selected by markets, 16-17 sellers accepted to join TB program through cross market SKUs migration or open a shop in SG/MY
3. Sellers who rejected and not selected by markets will be pitched via CNSIP [ETA: Jul]

3 [TB Top Sellers F&B Acquisition]: Out of 12 sellers acquired from top TB sellers list, SG/MY/TH selected all sellers to be pitched to join TB program

Table: TB Top Sellers F&B Acquisition Progress

Status	SG	MY	TH
1 Pitched #		152	
... Onboarded to SHP		12	
…… Selected by markets	12	12	12
…… Pending pitching to join program	12	12	12
... Seller Rejected		12	
... In Discussion		9	
... On Ice		119	

Highlights

1 Out of 152 top sellers pitched, 12 sellers acquired, all sellers are selected by SG/MY/TH to be pitched to join TB program [ETA: 25 Jun]

- Rejected sellers will be pitched to join via CNSIP
- Next steps: SAI team to be pitching to sellers out of the top TB sellers wishlist

Beauty Update

[Beauty Progress: existing program seller] Existing sellers pitching completed for SG/MY, in progress for VN/TW [ETA: 25 Jun]; TH pending incentives alignment [ETA: 24 Jun]

Completed | In progress | Planned, to start | Delayed

Market	Topic	#	Task	PIC	Status
[Migration] - Cross-migrate existing TB SKUs on Shopee platform					
SG	Commercial	4	Align potential migration pool	Kaiwen	Completed
		5	Align migration incentive plan to seller and marketing	Max	Completed
		6	Align SKUs migration target and ADO target	SG PIC/Jolene	In Progress
		7	Conduct seller pitching	Jolene	Completed
		8	Support seller onboarding / SKU listing	Jolene	In Progress
		9	Conduct marketing push	Kaiwen	To start
MY	Commercial	10	Align potential migration pool	Kaiwen	Completed
		11	Align migration incentive plan to seller and marketing	Max	Completed
		12	Align SKUs migration target and ADO target	SG PIC/Jolene	In Progress
		13	Conduct seller pitching	Jolene	Completed
		14	Support seller onboarding / SKU listing	Jolene	In Progress
		15	Conduct marketing push	Kaiwen	To start
TH	Commercial	16	Align potential migration pool	Nut	Completed
		17	Align migration incentive plan to seller and marketing	Nicholas	Delayed
		18	Align SKUs migration target and ADO target	TH PIC/Jolene	In Progress
		19	Conduct seller pitching	Jolene	To start
		20	Support seller onboarding / SKU listing	Jolene	To start
		21	Conduct marketing push	Nut	To start
VN	Commercial	22	Align potential migration pool	Summer	Completed
		23	Align migration incentive plan to seller and marketing	Nicholas	Completed
		24	Align SKUs migration target and ADO target	Summer	In Progress
		25	Conduct seller pitching	Jolene	In Progress
		26	Support seller onboarding / SKU listing	Jolene	To start
		27	Conduct marketing push	VN PIC/Jolene	To start
TW	Commercial	28	Align potential migration pool	Min Hui	Completed
		29	Align migration incentive plan to seller and marketing	Nicholas	Completed
		30	Align SKUs migration target and ADO target	Min Hui/Jolene	In Progress
		31	Conduct seller pitching	Jolene	In Progress
		32	Support seller onboarding / SKU listing	Jolene	To start
		33	Conduct marketing push	Min Hui	To start

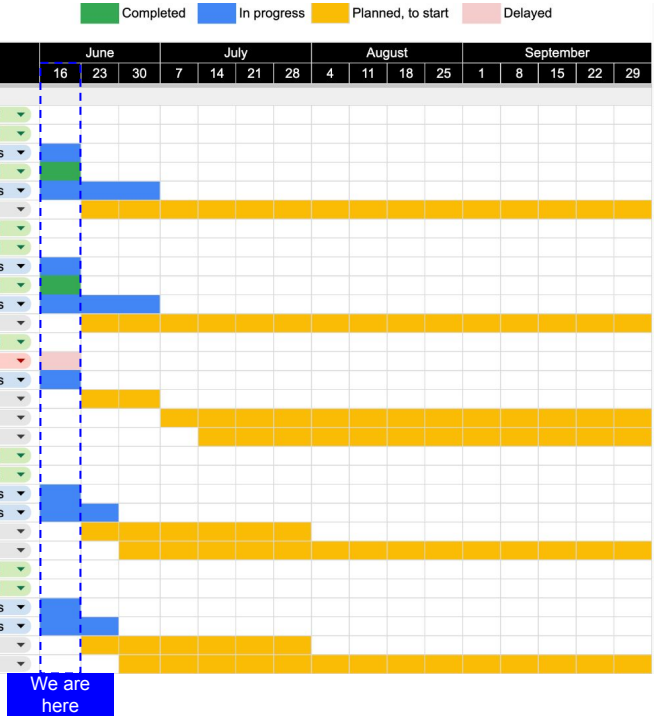

Highlights

- **Incentive Package Alignment (for all initiatives)**
  - SG, MY, VN, TW approved
  - Delay in for TH, pending budget approval and incentive confirmation ETA 24 Jun
- **Existing SHP TB sellers:** 52 TB sellers on SHP identified (after removing uncontactable sellers)
  - SG/MY selected 38 sellers (73%); 13 and 16 sellers accepted to join program respectively. Migration in progress [ETA: end Jun]
  - VN/TW pitching in progress [ETA: 25 Jun]
  - TH pending budget approval and incentive alignment ETA 24 Jun

[Beauty Progress: new top TB seller acquisition] 40 sellers acquired from top 300 TB sellers, to pitch them to join each mkt's program and push by Jul

Completed | In progress | Planned, to start | Delayed

Market	Topic	#	Task	PIC	Status
[Acquisition] - Acquire top TB sellers / SKUs that are not on SHP					
SG	Commercial	34	Identify TB Top 200 sellers	Keith	Completed
		35	Marketing resource alignment	Max	Completed
		36	Conduct seller pitching	Jolene	In Progress
		37	Seller onboarding and SKU listing/migration	Jolene	In Progress
		38	Marketing push	Kaiwen	To start
MY	Commercial	39	Identify TB Top 200 sellers	Keith	Completed
		40	Marketing resource alignment	Max	Completed
		41	Conduct seller pitching	Jolene	In Progress
		42	Seller onboarding and SKU listing/migration	Jolene	In Progress
		43	Marketing push	Kaiwen	To start
TH	Commercial	44	Identify TB Top 200 sellers	Keith	Completed
		45	Marketing resource alignment	Nicholas	Delayed
		46	Conduct seller pitching	Jolene	In Progress
		47	Seller onboarding and SKU listing/migration	Jolene	In Progress
		48	Marketing push	Nut	To start
VN	Commercial	49	Identify TB Top 200 sellers	Keith	Completed
		50	Marketing resource alignment	Nicholas	In Progress
		51	Conduct seller pitching	Jolene	In Progress
		52	Seller onboarding and SKU listing/migration	Jolene	In Progress
		53	Marketing push	Summer	To start
TW	Commercial	54	Identify TB Top 200 sellers	Keith	Completed
		55	Marketing resource alignment	Nicholas	In Progress
		56	Conduct seller pitching	Jolene	In Progress
		57	Seller onboarding and SKU listing/migration	Jolene	In Progress
		58	Marketing push	Min Hui	To start

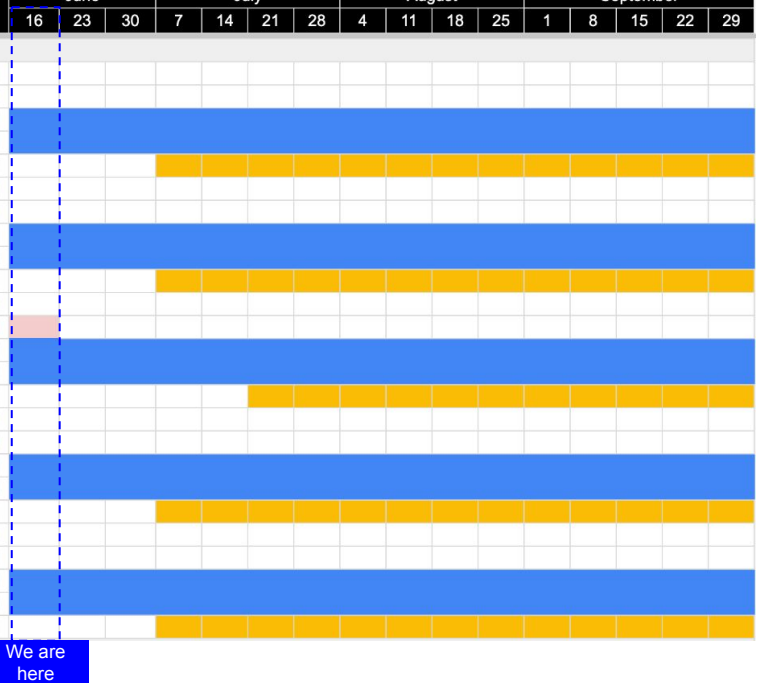

Highlights

- Pitching for top 300 TB sellers have concluded with 40 sellers onboarded onto SHP - to pitch for them to join program [ETA: 25 Jun]
- Next step: SAI team to be pitching to sellers outside of the top TB sellers wishlist in subsequent months (targets to be aligned by EOW)

[Beauty Progress: sourcing] Pitching ongoing and to conclude by 25 Jun, adding +0.7-2.4k new to SHP SKUs per market; to push in Jul

Completed | In progress | Planned, to start | Delayed

Market	Topic	#	Task	PIC	Status
[Sourcing] - Crawl and match top TB SKUs on SHP; Source those unmatched on SHP					
SG	Commercial	59	Crawl TB Top SKUs	Keith	Completed
		60	Mapping to existing SHP SKUs	Keith	Completed
		61	Curate regional sourcing wishlist	Jason	Completed
		62	SCS/Lovito/CN Sellers/SIP to source	Max/Nicholas	In Progress
		63	Marketing resource alignment	Max	Completed
		64	SKUs review	Kaiwen	To start
		65	Marketing push	Kaiwen	To start
MY	Commercial	70	Crawl TB Top SKUs	Keith	Completed
		71	Mapping to existing SHP SKUs	Keith	Completed
		72	Curate regional sourcing wishlist	Jason	Completed
		73	SCS/Lovito/CN Sellers/SIP to source	Max/Nicholas	In Progress
		74	Marketing resource alignment	Max	Completed
		75	SKUs review	Kaiwen	To start
		76	Marketing push	Kaiwen	To start
TH	Commercial	81	Crawl TB Top SKUs	Keith	Completed
		82	Mapping to existing SHP SKUs	Keith	Completed
		83	Curate regional sourcing wishlist	Jason	Completed
		84	SCS/Lovito/CN Sellers/SIP to source	Max/Nicholas	In Progress
		85	Marketing resource alignment	Nicholas	Delayed
		86	SKUs review	Nut	To start
		87	Marketing push	Nut	To start
VN	Commercial	92	Crawl TB Top SKUs	Keith	Completed
		93	Mapping to existing SHP SKUs	Keith	Completed
		94	Curate regional sourcing wishlist	Jason	Completed
		95	SCS/Lovito/CN Sellers/SIP to source	Max/Nicholas	In Progress
		96	Marketing resource alignment	Nicholas	Completed
		97	SKUs review	Summer	To start
		98	Marketing push	Summer	To start
TW	Commercial	103	Crawl TB Top SKUs	Keith	Completed
		104	Mapping to existing SHP SKUs	Keith	Completed
		105	Curate regional sourcing wishlist	Jason	Completed
		106	SCS/Lovito/CN Sellers/SIP to source	Max/Nicholas	Paused
		107	Marketing resource alignment	Nicholas	Paused
		108	SKUs review	Min Hui	Paused
		109	Marketing push	Min Hui	Paused

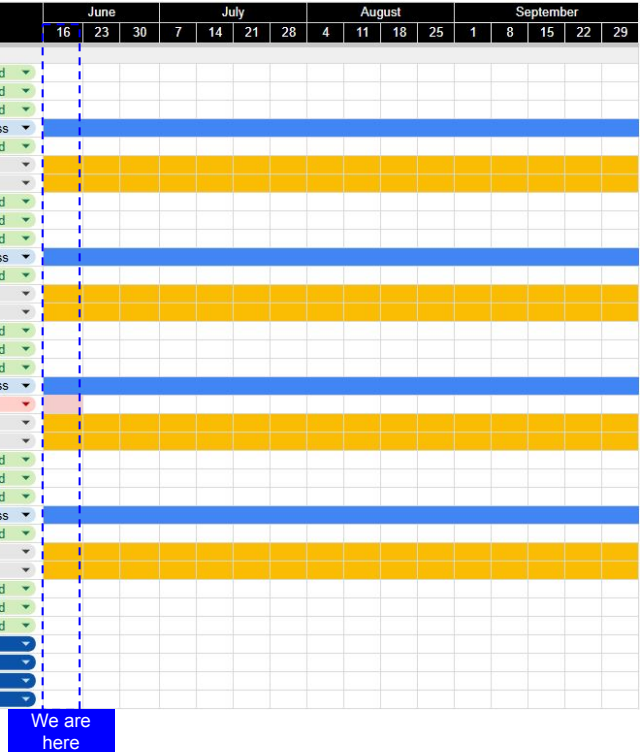

Highlights

- June current pitching results in (as of 17 Jun) - 744 (SG), 1,375 (MY), 2,401 (TH), 1,502 (VN)
- Delay in SKUs review due to longer time required to clean up seller nomination sheet; To be shared to markets after clean up on 25 Jun and get markets to select by 30 Jun
- SCS targets alignment in progress; to official start in Aug

[Beauty] Overview of initiatives: Acquired 13-16 sellers sellers to join program and start migration for SG/MY; acquired 40 out of top 300 TB Beauty sellers

Domain	#	Initiative	Market	Status
Grow SKU count through migration, acquisition, sourcing, ERP	1	Cross-market SKU migration	SG/MY/TH/VN/TW	• SG/MY: 13/38 and 16/38 sellers accepted to join program via migration/shop opening for SG and MY respectively; SKUs migration in progress [ETA: end Jun] • VN/TW: Pitching for migration in progress, first round of results on 25 Jun • TH: Pending budget approval and incentive alignment ETA 24 Jun; To complete pitching by 2 Jul Deep-dive
	2	SKU sourcing	SG/MY/TH/VN	• SG/MY/TH/VN: June current pitching results in (as of 17 Jun) - 744 (SG), 1,375 (MY), 2,401 (TH), 1,502 (VN). To pass to markets for review by 30 Jun after clean up of seller SKU nomination list
	3	TB seller acquisition	SG/MY/TH/VN/TW	• SG/MY: Acquisition pitching for top 300 TB sellers concluded with 40 sellers onboarded onto SHP, to pitch for them to join program [ETA: 25 Jun] • VN/TW: Pitching in progress [ETA: 25 Jun] • TH: Pending incentive alignment ETA 24 Jun; To complete pitching by by 2 Jul Deep-dive
	4	TB seller self-nomination	SG/MY/TH/VN/TW	• To start seller broadcasting on 11 Jun via 9 channels including CNSC banner, SEH announcement, social media, etc; First round of results by 20 Jun

1 [Beauty Existing Sellers Pitching Progress] Out of 38 sellers selected by markets, 13-16 sellers accepted to join program via migration/shop opening in SG/MY; migration of SKUs started and to complete by end Jun

Table: Beauty Existing Sellers Pitching Progress

	Status	SG			MY			Remarks
		Seller #	SKU #	ADO	Seller #	SKU #	ADO	
1	Pitching Pool	52	1,192	341	52	1,438	918	
	(1) Selected by market	**38**	**1,172**	**341**	**38**	**1,315**	**906**	
2	... Accepted	13	622	244	16	755	608	SKUs migration started this week, complete migration by end Jun
	... Pending to accept via migration tool	15	429	84	14	557	298	Invited to migrate via migration tool [ETA: 27 Jun]
3	... Rejected	10	121	13	8	3	0	
	(2) Not selected by market	**14**	**20**	**0**	**14**	**123**	**13**	

Highlights

1. A total of 52 TB sellers from existing SHP pool are identified for pitching; with 1.2k and 1.4k SKUs and 341 and 918 ADO in SG/MY respectively
2. Of the 38 sellers selected by markets, 13-16 sellers accepted to join TB program through cross market SKUs migration or open a shop in SG/MY
3. Sellers who rejected and not selected by markets will be pitched via CNSIP [ETA: Jul]

3 [TB Top Sellers Beauty Acquisition]: Out of 40 acquired sellers from TB Top sellers, markets selected 16-31 sellers to pitch for them to join TB program; 5-14 sellers not selected will be pitched via CNSIP

Table: TB Top Sellers Beauty Acquisition Progress

Status	SG	MY	TH	VN	TW
Pitched #			247		
... Onboarded to SHP			40		
1 **(1) Selected by markets**	17	25	31	21	16
... Pending pitching to join program	17	25	31	21	16
2 **(2) Not selected by markets, pitch CNSIP**	14	5	0	10	0
(3) Not selected by markets due to existing similar brands in mkt	9	10	9	9	24
... Seller Rejected			23		
... In Discussion			8		
... On Ice			176		

Highlights

1. Out of 40 acquired sellers, 16-31 sellers have been selected across markets and will be pitched to join program [ETA: 25 Jun]
2. Sellers not selected by markets (not due to having existing presence in mkt) will be pitched via CNSIP [ETA: Jul]

- Next steps: SAI team to be pitching to sellers out of the top TB sellers wishlist to meet the target of xx each month from Jul onwards
